

Weekly Research Update

Single Project Progress Report

Muting (Don) Ma

September 15, 2026

Bi-objective Intersection Paper Revision

Component Rebuild and First Production Attempt

Public artifacts: [OpenProjects repository](#)

This report covers one project, the revision of the bi-objective connected and automated vehicle intersection manuscript, since the September 8, 2026 meeting. Its five sections follow the requested update format, and every claim traces to the commit history of the manuscript repository, the new runtime package, and the retired legacy codebase. The referenced works follow the five sections.

Contents

1	Current Objective	1
2	Progress Since the Last Meeting	2
3	Key Result or Lesson	3
4	Input Needed from Dr. Gong	4
5	Before the Next Meeting	5
	References	6

1. Current Objective

Name: Muting (Don) Ma**Project:** Bi-objective Intersection Paper Revision**Date:** September 15, 2026

Context. At a reservation-based intersection, the manuscript schedules connected and automated vehicles by trading average speed against priced collision risk [2]. The September 8, 2026 comments name the experiments as the remaining concern and retarget the paper from Transportation Research Part C to Transportation Research Record or the Journal of Intelligent Transportation Systems [1]. The six requested experiments are stochastic timing errors on every trajectory, at least thirty seeds per configuration, synchronized, random, and platooned arrivals, one, two, and three vehicles per lane with rear-end exposure admitted, turning splits of 25, 50, and 75 percent, and stronger baselines. The deliverable is therefore the evidence, not the exposition, and the baseline set carries six controller classes with the published speed-maximization method mapped onto the delay-only class [3].

1.1 Objective


- Deliver the six experiments of the September 8 note as schedules that are certified optimal, independently validated, and reproducible from saved artifacts.

2. Progress Since the Last Meeting

- **Completed:** Expanded the six requested experiments into seven cases by thirty seeds by twenty-one rows, which is 4,410 report rows, then rebuilt the study as eleven component contracts and a matching `biobj` runtime package, retiring the legacy BiCAVO codebase after its audit against that plan.
- **Completed:** Replaced the rear-end time-to-collision surrogate with a priced contact probability, replaced the thousand draw replay with exact expectations at each timing error width, and widened initial following gaps to hold modeled contact risk at or below 0.1 percent.
- **Blocked:** The first production campaign ran twelve workers for 2 hours and 52 minutes and was stopped: 14 of 4,410 report rows were saved, and 13 of those 14 fail the independent validator.

3. Key Result or Lesson

- Every saved solve is certified optimal at a zero optimality gap, yet recounting its own trajectory places two vehicles in one conflict cell and raises the crossing count by 2 to 6, so the model's occupancy constraints and the validator's recount do not agree.
- Solving to a zero gap does not scale: the launched settings project 802 days to finish the design, with a 10th to 90th percentile range of 654 to 1,125 days.
- Restricting the campaign to the five eight-vehicle cases projects 43 days, and a one hour limit per solve projects 10 days, which makes the gap policy, not the hardware, the binding choice.

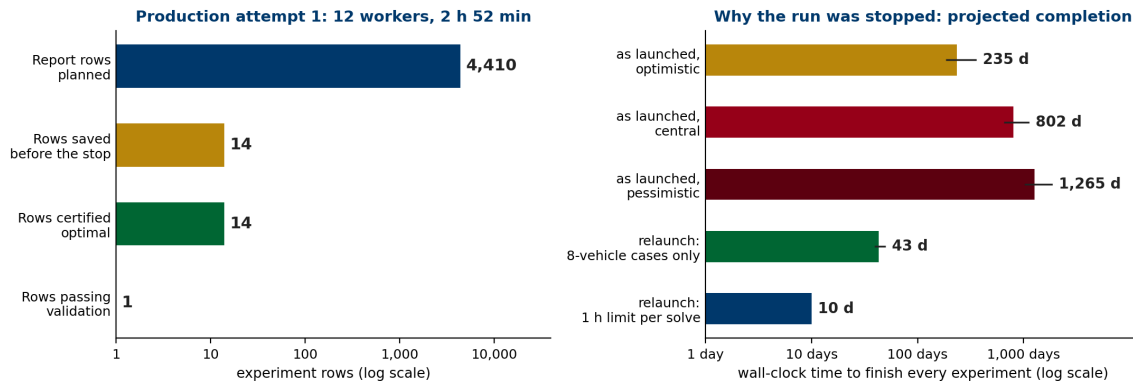

Left: 14 rows saved, every solve certified optimal at zero gap, 13 failed the independent validator. Right: median of 300 simulated scheduler runs; line spans the 10th to 90th percentile.

Figure 1: Saved rows of the first production attempt and the projected time to finish the full design.

4. Input Needed from Dr. Gong

- Should the reconciliation in [Section 3](#) change the model's cell occupancy constraints, or the validator's recount of the saved trajectory?
- Should the sixteen and twenty-four vehicle cases carry a per-solve time limit with reported bounds and gaps, or remain at a zero gap at the cost of the schedule in [Fig. 1](#)?

5. Before the Next Meeting

- Reconcile occupancy and crossing counts between the model and the validator at the production 0.1 second time step.
- Relaunch the five eight-vehicle cases, writing rows to local disk and copying finished rows to the synced folder with retries.
- Report per-row bounds, gaps, and validation outcomes for every relaunched row.

Public artifacts: [project folder](#); [selected snapshot](#).

References

- [1] J. Gong, “Re: TRC manuscript status and help needed for submission,” comments on the manuscript experiments and submission venue, September 8, 2026. Held locally as `Comments/Gong/20260908/TRRComments.pdf` in the manuscript repository.
- [2] M. Ma and M. Yavuz, “Socioeconomic Tradeoff on Connected and Automated Vehicles Scheduling at a Reservation-based Intersection,” Social Science Research Network, 2025. [doi:10.2139/ssrn.5372729](https://doi.org/10.2139/ssrn.5372729).
- [3] M. Ma and Z. Li, “A Speed-Maximization Trajectory Optimization Model on a Reservation-Based Intersection Control System,” *Transportation Research Part C: Emerging Technologies*, vol. 154, art. 104266, 2023. [doi:10.1016/j.trc.2023.104266](https://doi.org/10.1016/j.trc.2023.104266).
